

# **SUPPLEMENTARY AGENDA 1**

---

Distributed on 9 August 2019



## **INNER WEST COUNCIL**

**COUNCIL MEETING**

**TUESDAY 13 AUGUST 2019**

**6.30pm**

---

Location Ashfield Service Centre, 260 Liverpool Road, Ashfield

**MEETING AGENDA – PRECIS  
SUPPLEMENTARY ITEMS**

The following report appear as late item with approval as information required for the preparation of the report was not available at the time of distribution of the Business Paper.

**1 Reports for Noting**

| <b>ITEM</b>                              | <b>Page</b> |
|--|-------------|
| C0819(1) Item 19 Update on Ashfield Pool | <b>3</b>    |

---

**Item No:** C0819(1) Item 19  
**Subject:** UPDATE ON ASHFIELD POOL  
**Prepared By:** Michael Deegan - Chief Executive Officer  
**Authorised By:** Michael Deegan - Chief Executive Officer

---

**RECOMMENDATION**

**THAT Council receive and note the report.**


---

**ATTACHMENTS**

1. [↓](#) Portfolio Report - Ashfield Pool

## IWC Portfolio Report

| IWC Cost Centre | Council Group | Financial Year | Project Name                  | Project Status | Public Project |
|-----------------|---------------|----------------|-------------------------------|----------------|----------------|
| All             | All           | All            | 18-19 Ashfield Aquatic Centre | All            | All            |

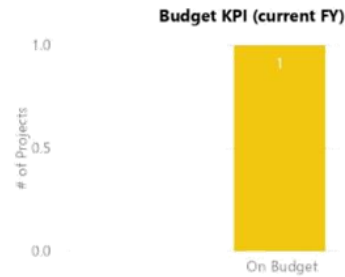

| Project Name                  | Project Status | % Complete | Latest Update Date | Current Status Update (Internal)  | Previous Status Update (Internal)   |
|-------------------------------|----------------|------------|--------------------|---|---|
| 18-19 Ashfield Aquatic Centre | In Progress    | 14         | 10/07/2019         | <ul style="list-style-type: none"> <li>- The site demolition work completed on 29 June 2019. The remaining wall structure of the old plant room will be kept to retain the railway embankment.</li> <li>- The excavation works of borrowing pit have commenced at Bastable Street Carpark under the supervision of both contractor's Geotechnical engineer and the environmental consultant</li> <li>- The piling work has recommenced after site set out issues and the continued wet weather conditions.</li> </ul> | <ul style="list-style-type: none"> <li>- The last building demolition works are nearing completion with only partial s remaining from the administration building and underground plant room near corridor.</li> <li>- Bulk earthworks have commenced. Borrowing pit will be proposed to buried material from earthwork that contained asbestos fragments.</li> <li>- Piling works to the new building have commenced on site.</li> </ul> |

**Current Status Update (Public)**

HAZMAT removal has completed with all air monitoring report indicating the air particle levels were below the thresholds from the demolition works.

**Previous Status Update (Public)**

The building demolition works and earthworks continue including removal of latent discoveries (bonded asbestos) under the supervision of independent hygienist. The hygienist has positioned the air monitoring stations around the work zone to ensure the best practice of the remedial works. The air monitoring results have been reviewed at the end of each workday.
